



OREGON

Debris Management
Task Force

Wildfire Debris & Hazard Tree Removal Update

HOUSE SPECIAL COMMITTEE ON WILDFIRE RECOVERY




MARCH 8, 2021



Weekly topline points | from the week of March 1-5

- Drier weather, more crews, and completed prep work helped add 55 cleared sites **for a total of 332 statewide** (out of 2,197 total home sites).
- Hazard tree work actively continues: **38,157 trees marked and 8,451 removed** of the nearly 290,000 estimated statewide.
- Crews began **removing debris near Glide** (Archie Creek) **and in Detroit** (Beachie Creek/Lionshead)
- **Helping Oregon communities** through our operations:
 - removing hazard trees next to the McKenzie School District campus so that classes can resume this month;
 - donating wood to families in need for heat in Jackson County;
 - quickly prioritized clearing two mobile home parks in Jackson County to allow for FEMA direct housing work
- **Challenges to note:** wet weather will return, planning for daily landfill capacity constraints, steep terrain in Archie Creek and elsewhere

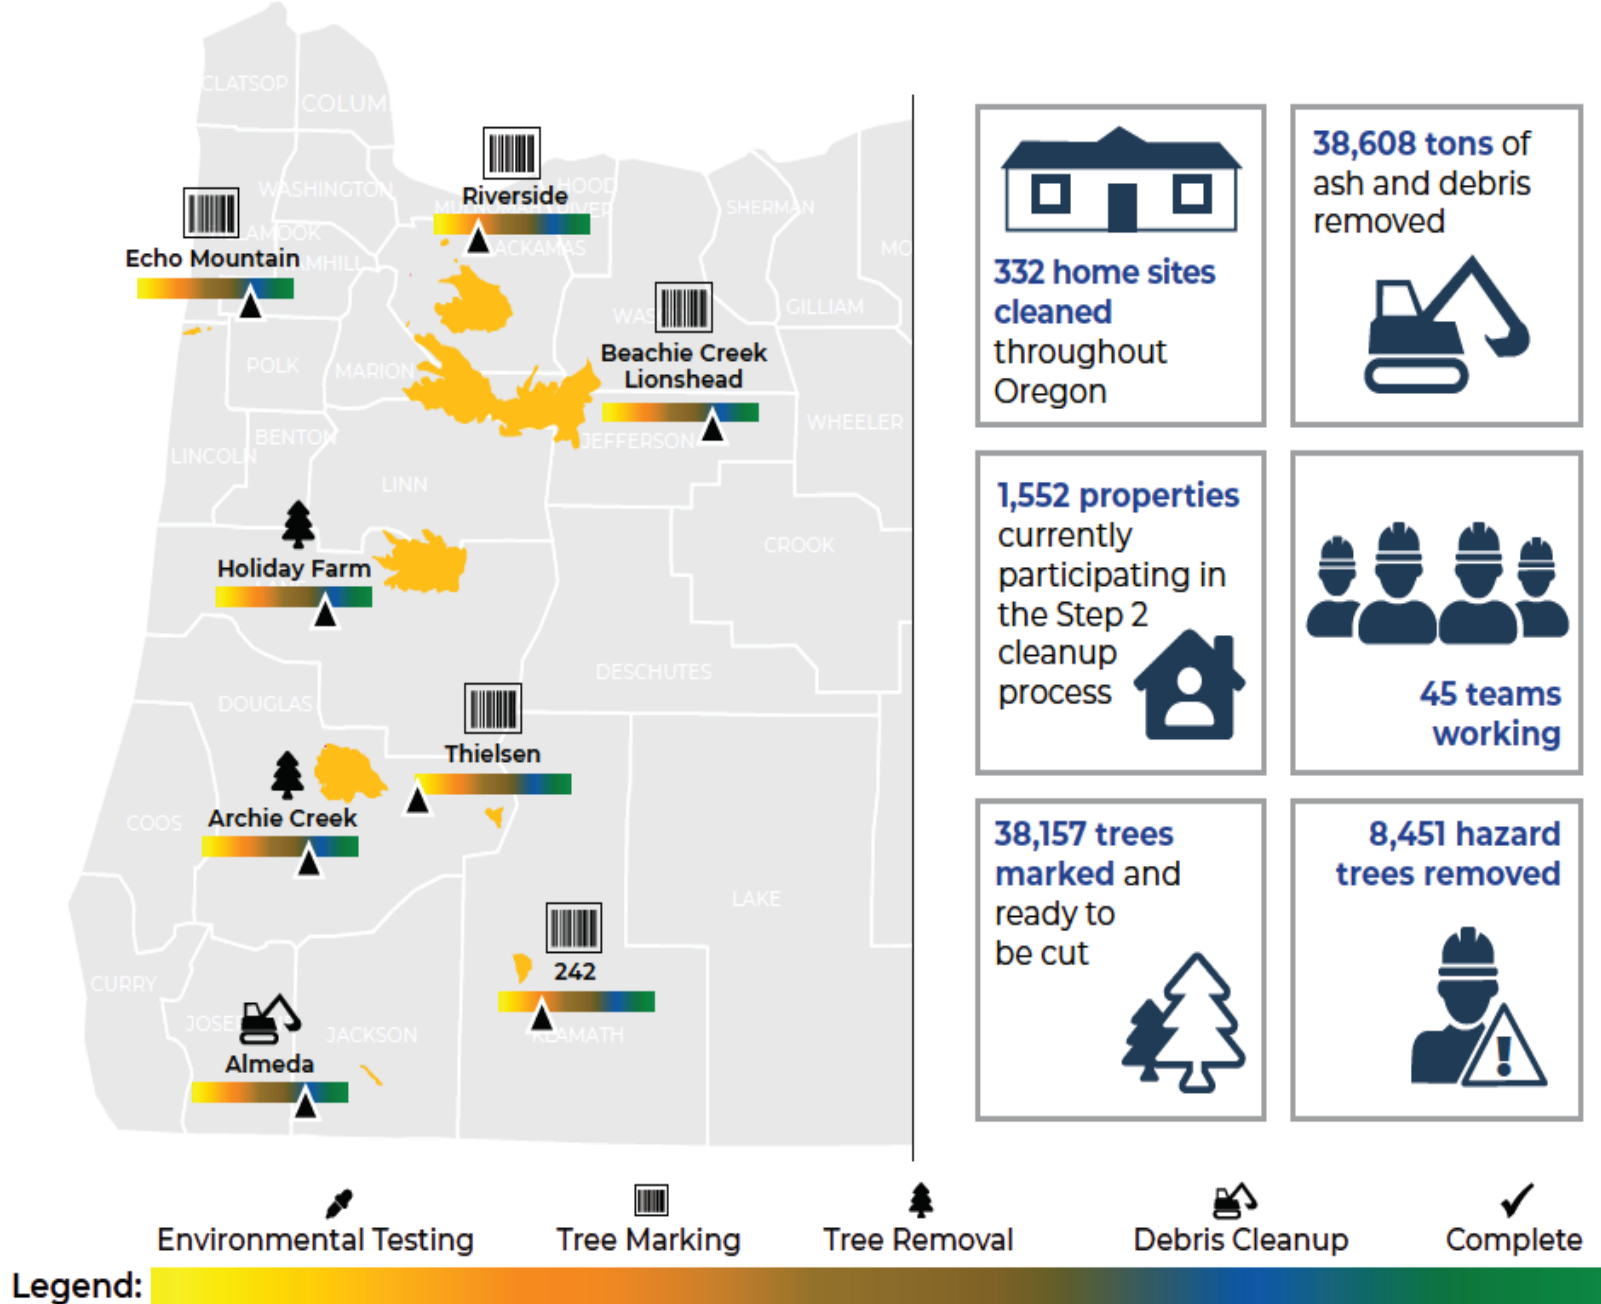

332 home sites
cleaned
throughout
Oregon

38,608 tons of
ash and debris
removed



1,552 properties
currently
participating in
the Step 2
cleanup
process



45 teams
working

38,157 trees
marked
and
ready to
be cut



8,451 hazard
trees removed




BY THE NUMBERS

As of Friday 3/5/21

- **Nearly 40,000 tons of debris removed** equals the weight of 3,000 school buses
- **1,552 properties participating** through complete Right of Entry forms (this number fluctuates).

Data dashboard by fire and interactive status map: <https://bit.ly/3bMyqBl>

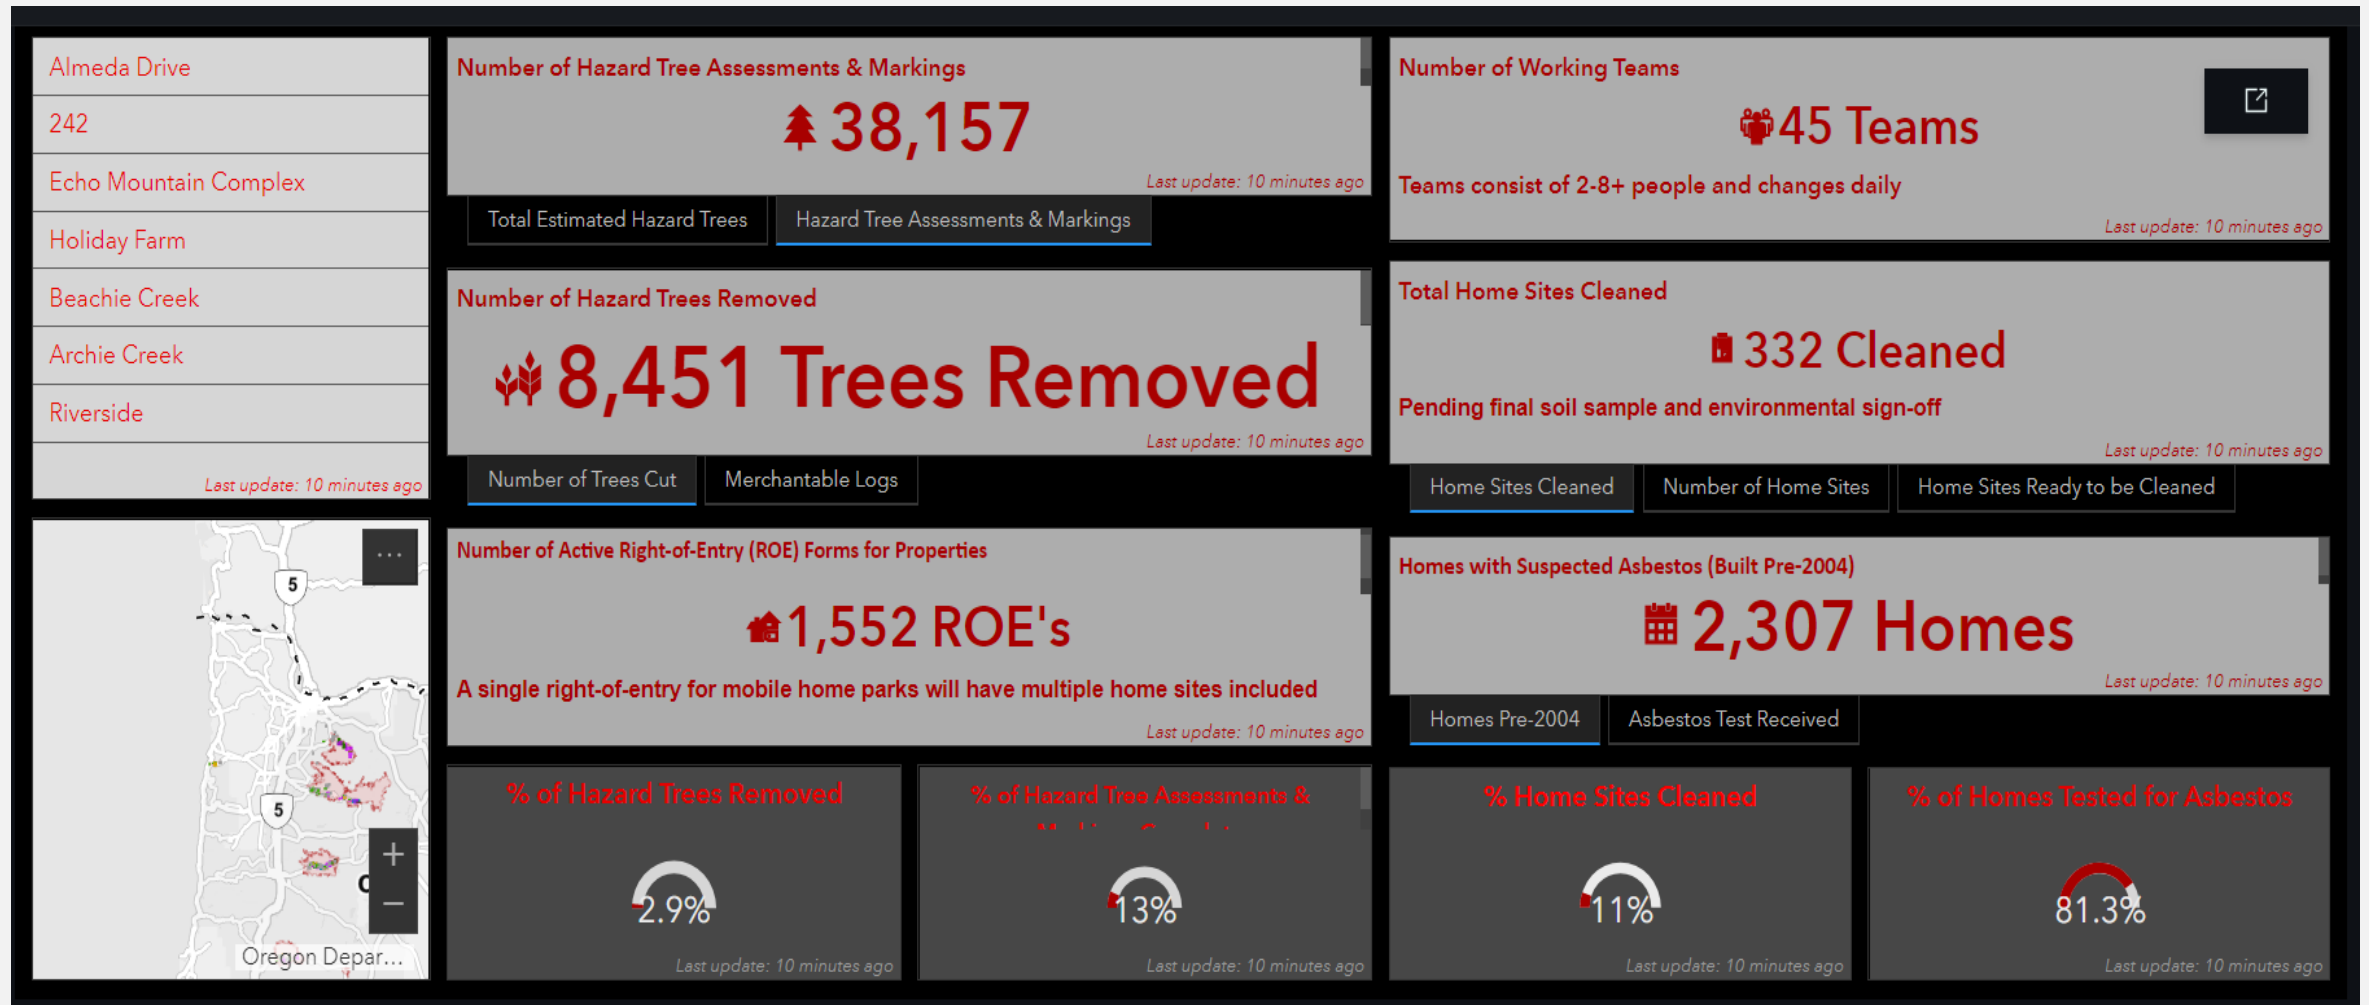

*Data captured on Friday, March 5

Looking ahead

ready sites in the next 3 weeks

Fire Area	Week 1 For week of March 8, 2021	Week 2	Week 3
<u>Alameda</u>	656 sites ready for cleanup	+ 62	+ 76 = 794/ out of 1,142 total sites
Archie Creek	22 sites ready for cleanup	+ 6	+ 16 = 44/ out of 75 total sites
<u>Beachie Creek</u>	32 sites ready for cleanup	+ 26	+ 33 = 91/ out of 560 total sites
Echo Mountain	79 sites ready for cleanup	+12	+ 14 = 105/ out of 117 total sites
Holiday Farm	26 sites ready for cleanup	+15	+ 45 = 86/ out of 270 total sites
Riverside	4 sites ready for cleanup	+ 8	+ 1 = 13/ out of 33 total sites
			Total = 1,133 out of 2,197 total sites

Track status with us



Youtube.com/OregonDOT



Twitter.com/OregonOEM



Flickr.com/oregondot

Webpage, interactive status map, dashboard
wildfire.oregon.gov/cleanup

Debris news page
www.DebrisCleanupNews.com



odot.wildfire@odot.state.or.us



Hotline: 503-934-1700
