


Wildfire Debris & Hazard Tree Removal Update


HOUSE SPECIAL COMMITTEE ON WILDFIRE RECOVERY



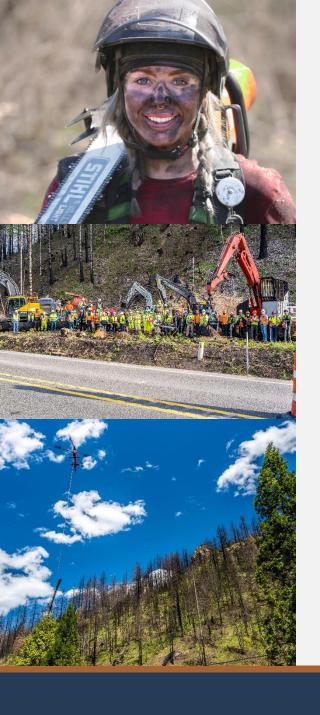

Weekly topline points | from the week of May 10-14

- We have passed the halfway point for participating home sites cleared. +153 cleared sites completed this week for a total of 1,816 statewide (out of 2,825 total home sites).
- 77,795 fire-damaged trees marked and 34,959 removed of the more than 140,000 estimated statewide. Trees are marked through a series of reviews and quality control measures.
- Independent arborist/forester contract finalized on Wednesday to provide independent review of operation and additional evaluation oversight.
- With significant progress continuing in all fire areas, Right-of-Entry deadlines will soon be announced in Clackamas and Lane counties.
- The hotline 503-934-1700 is always available to help answer questions and coordinate concerns. Property calls about debris removal and ROEs make up majority of calls.

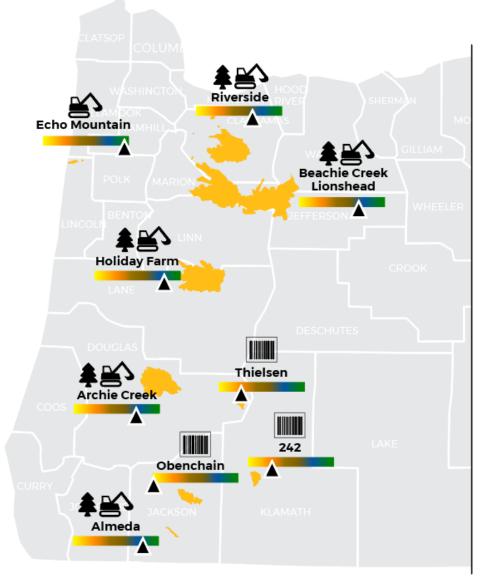

Legend:











1,117 people in the workforce. 65% from Oregon

156 firms performing cleanup, 141 are Oregon-based, 74 certified small businesses




BY THE NUMBERS


As of Thursday 5/13/21

- **1,429 properties** and 2,825 home sites participating through complete Right of Entry forms (this number fluctuates).
- Number of crews working: 96 contractor crews, 59 monitoring crews currently working.
- **Data dashboard** by fire and interactive status map: https://bit.ly/3bMyqBl

Hazard Tree Removal and Private Property Debris Removal look ahead: northern Oregon

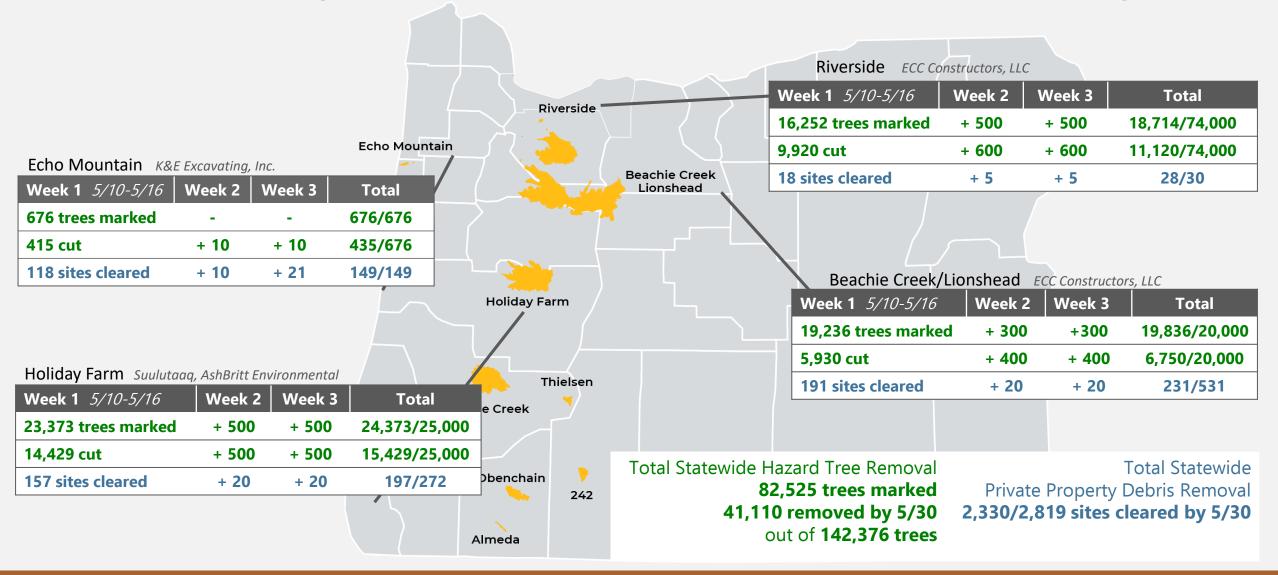

Hazard Tree Removal and Private Property Debris Removal look ahead: southern Oregon

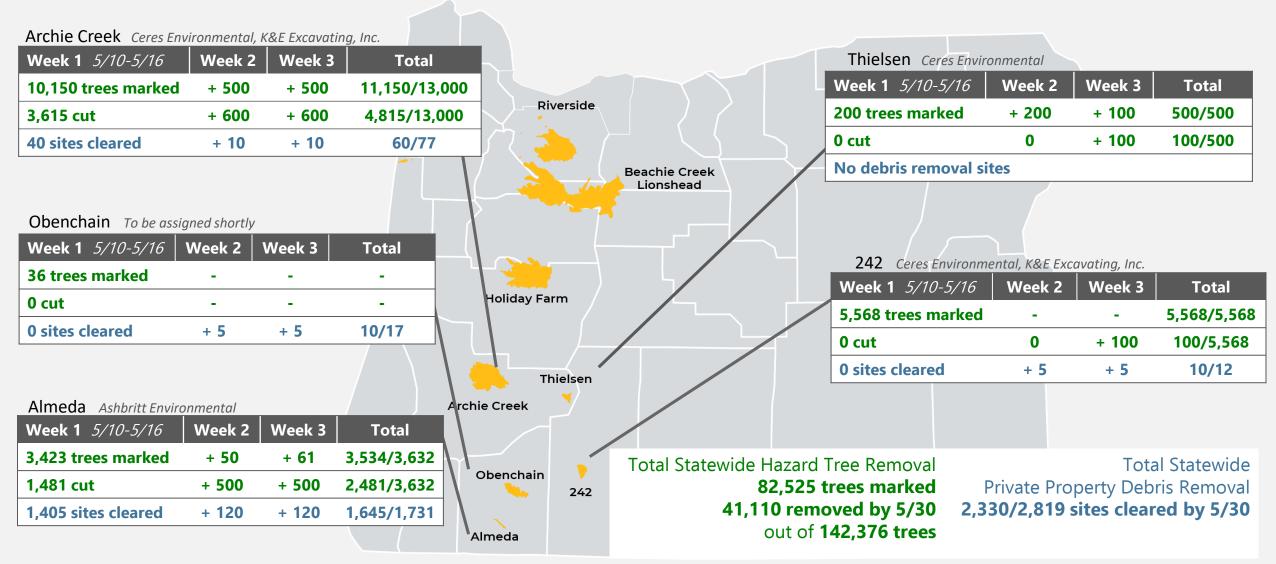

Track status with us

Webpage, interactive status map, dashboard wildfire.oregon.gov/cleanup

Debris news page www.DebrisCleanupNews.com



Youtube.com/OregonDOT



Twitter.com/OregonOEM



Flickr.com/oregondot



odot.wildfire@odot.state.or.us



Hotline: 503-934-1700
