



OREGON

Debris Management
Task Force

Wildfire Debris & Hazard Tree Removal Update

HOUSE SPECIAL COMMITTEE ON WILDFIRE RECOVERY




MAY 28, 2021



Weekly topline points | from the week of May 24-28

- **We have passed the halfway point for participating home sites cleared. +87 cleared sites completed this week for a total of 1,966 statewide** (out of 2,831 total home sites).
- **80,604 fire-damaged trees marked and 39,098 removed** of the more than 140,000 estimated statewide. Trees are marked through a series of reviews and quality control measures.
- **Review of hazard tree operation underway by an Independent arborist.** Field work completed with final report expected in early June and we look forward to learning more about any potential recommendations.
- **Know before you go this Memorial Day.** Along with TripCheck, add Oregon's [recreation site status map](#) to your resource list. It's a must-check, one-stop shop for anyone exploring the outdoors this summer.
- **The deadline to apply for property cleanup is approaching.** We want to give everyone with wildfire damaged properties the opportunity to participate in the state-led cleanup program.

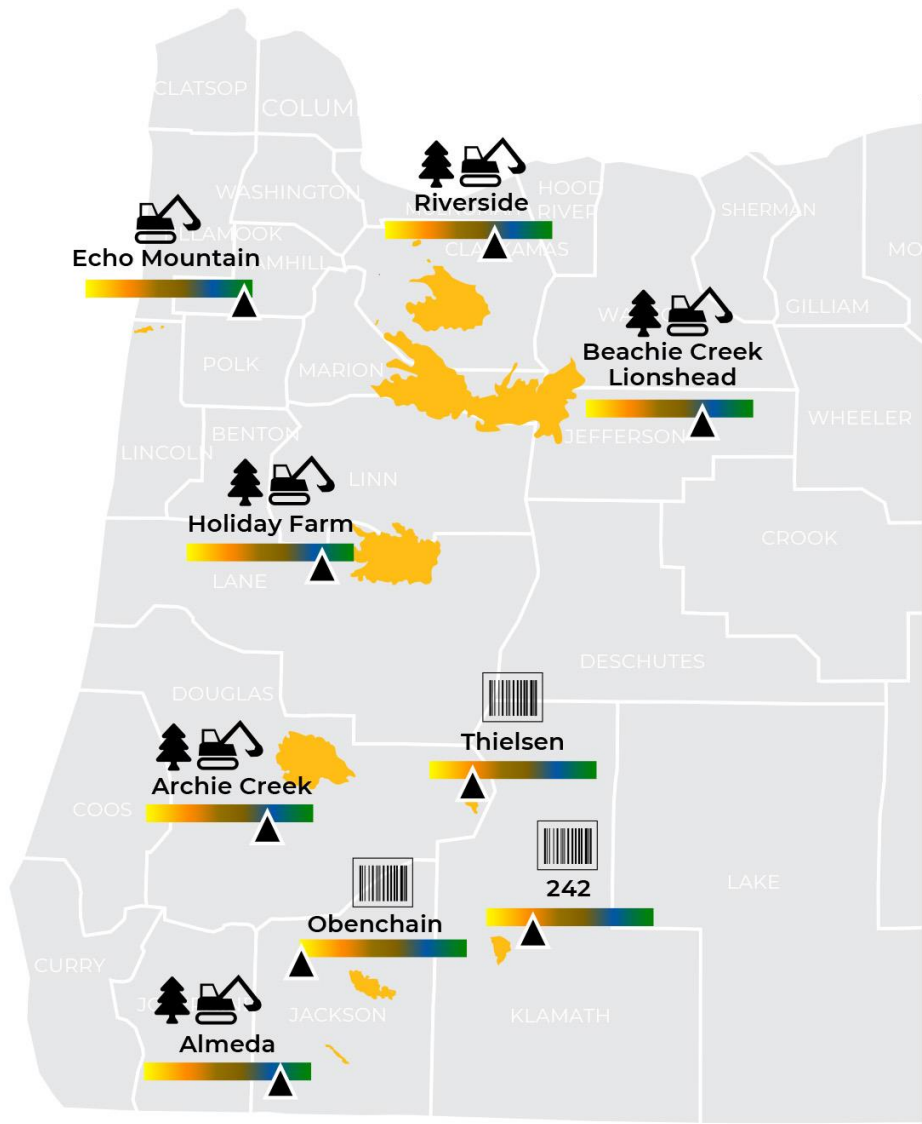


1,966 home sites
 cleared
 throughout
 Oregon

1,396 properties
 and **2,831 home**
sites currently
 participating in
 the Step 2
 cleanup 
 process

80,604 trees
marked and
 ready to
 be cut


39,098 hazard
trees removed



1,207 people
 in the workforce,
67% from Oregon

167 firms 
 performing
 cleanup, **151** are
Oregon-based,
85 certified small
 businesses


BY THE NUMBERS

As of Thursday 5/27/21

- **1,396 properties and 2,831 home sites participating** through complete Right of Entry forms (this number fluctuates).
- **Number of crews working:**
 65 contractor crews,
 52 monitoring crews
 currently working.
- **Data dashboard** by fire and interactive status map:
<https://bit.ly/3bMyqBl>



Hazard Tree Removal and Private Property Debris Removal look ahead: northern Oregon

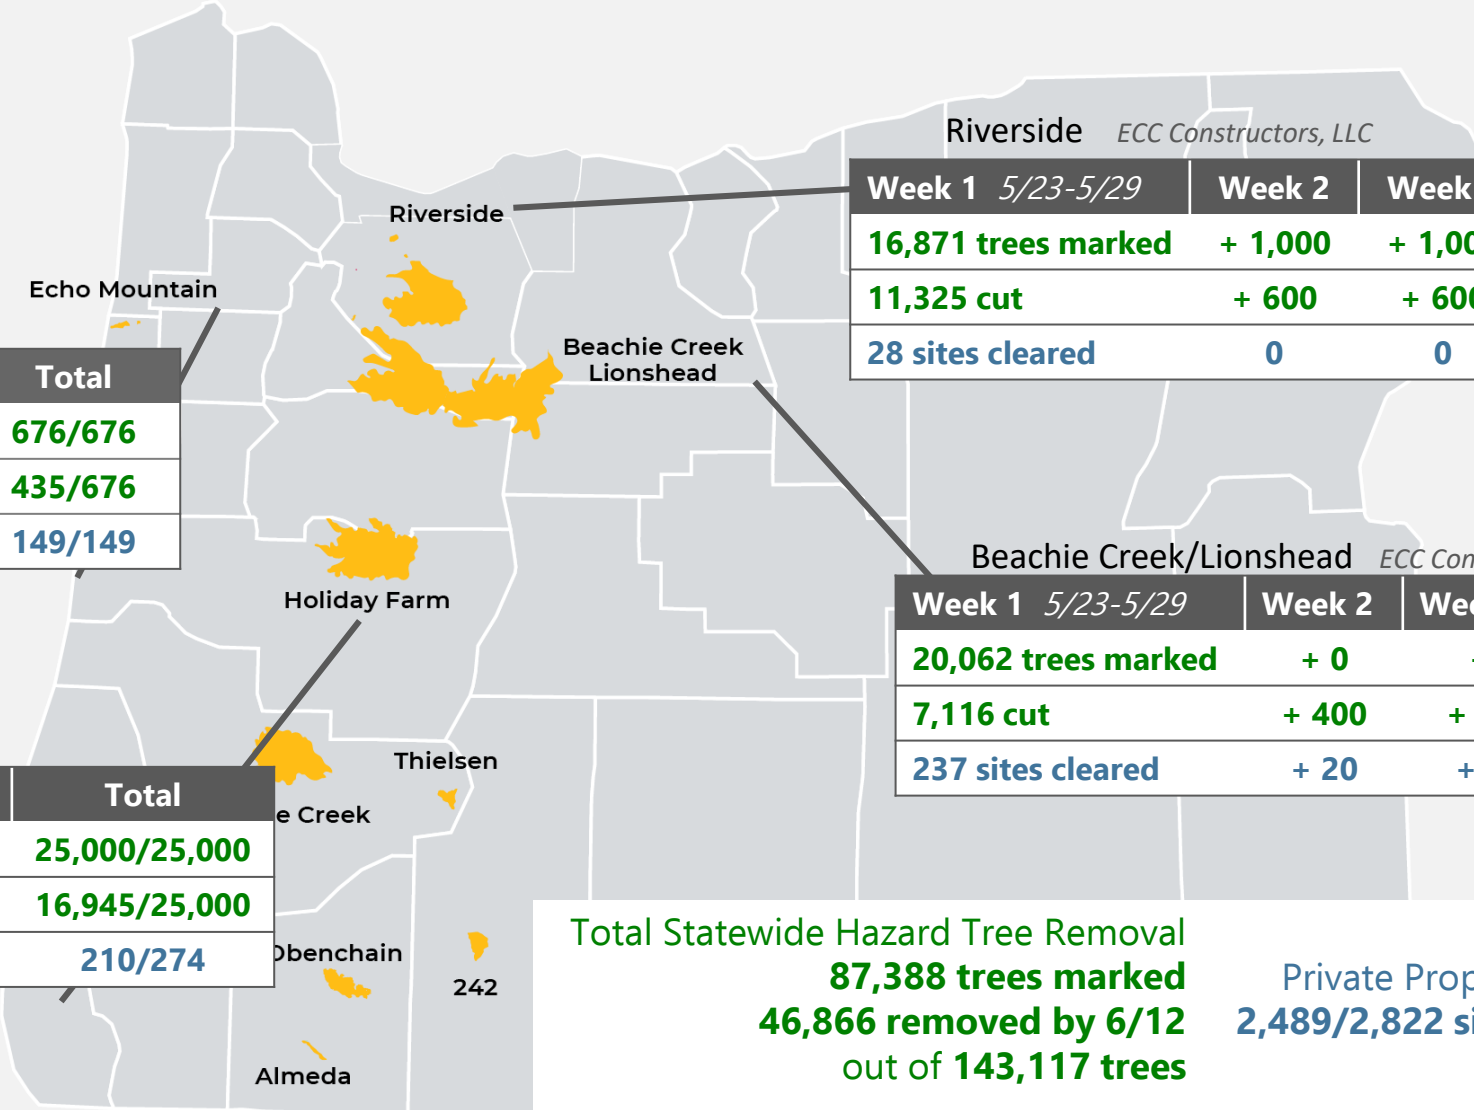

Echo Mountain *K&E Excavating, Inc.*

Week 1 5/23-5/29	Week 2	Week 3	Total
676 trees marked	-	-	676/676
415 cut	+ 10	+ 10	435/676
149 sites cleared	0	0	149/149

Riverside *ECC Constructors, LLC*

Week 1 5/23-5/29	Week 2	Week 3	Total
16,871 trees marked	+ 1,000	+ 1,000	18,871/74,334
11,325 cut	+ 600	+ 600	12,525/74,334
28 sites cleared	0	0	28/28

Beachie Creek/Lionshead *ECC Constructors, LLC*

Week 1 5/23-5/29	Week 2	Week 3	Total
20,062 trees marked	+ 0	+ 0	20,062/20,100
7,116 cut	+ 400	+ 400	7,916/20,100
237 sites cleared	+ 20	+ 20	277/526

Holiday Farm *Suulutaag, AshBritt Environmental*

Week 1 5/23-5/29	Week 2	Week 3	Total
24,182 trees marked	+ 500	+ 318	25,000/25,000
15,945 cut	+ 500	+ 500	16,945/25,000
170 sites cleared	+ 20	+ 20	210/274

Total Statewide Hazard Tree Removal
87,388 trees marked
46,866 removed by 6/12
 out of **143,117 trees**

Total Statewide Private Property Debris Removal
2,489/2,822 sites cleared by 6/12

Hazard Tree Removal and Private Property Debris Removal look ahead: southern Oregon

Archie Creek *Ceres Environmental, K&E Excavating, Inc.*

Week 1 5/23-5/29	Week 2	Week 3	Total
10,385 trees marked	+ 500	+ 400	11,285/11,815
3,747 cut	+ 600	+ 600	4,947/11,815
46 sites cleared	+ 10	+ 10	66/77

Obenchain *To be assigned shortly*

Week 1 5/23-5/29	Week 2	Week 3	Total
-	-	-	-
-	-	-	-
0 sites cleared	+ 5	+ 5	10/17

Alameda *Ashbritt Environmental*


Week 1 5/23-5/29	Week 2	Week 3	Total
3,611 trees marked	+ 21	0	3,632/3,632
2,348 cut	+ 500	+ 500	3,348/3,632
1,519 sites cleared	+ 110	+ 110	1,739/1,739

Thielsen *Ceres Environmental*

Week 1 5/23-5/29	Week 2	Week 3	Total
1,502 trees marked	+ 200	+ 200	1,902/2,000
0 cut	0	+ 650	650/2,000
No debris removal sites	-	-	-

242 *Ceres Environmental, K&E Excavating, Inc.*

Week 1 5/23-5/29	Week 2	Week 3	Total
5,960 trees marked	0	0	5,960/5,960
0 cut	0	+ 100	100/5,960
0 sites cleared	+ 5	+ 5	10/12

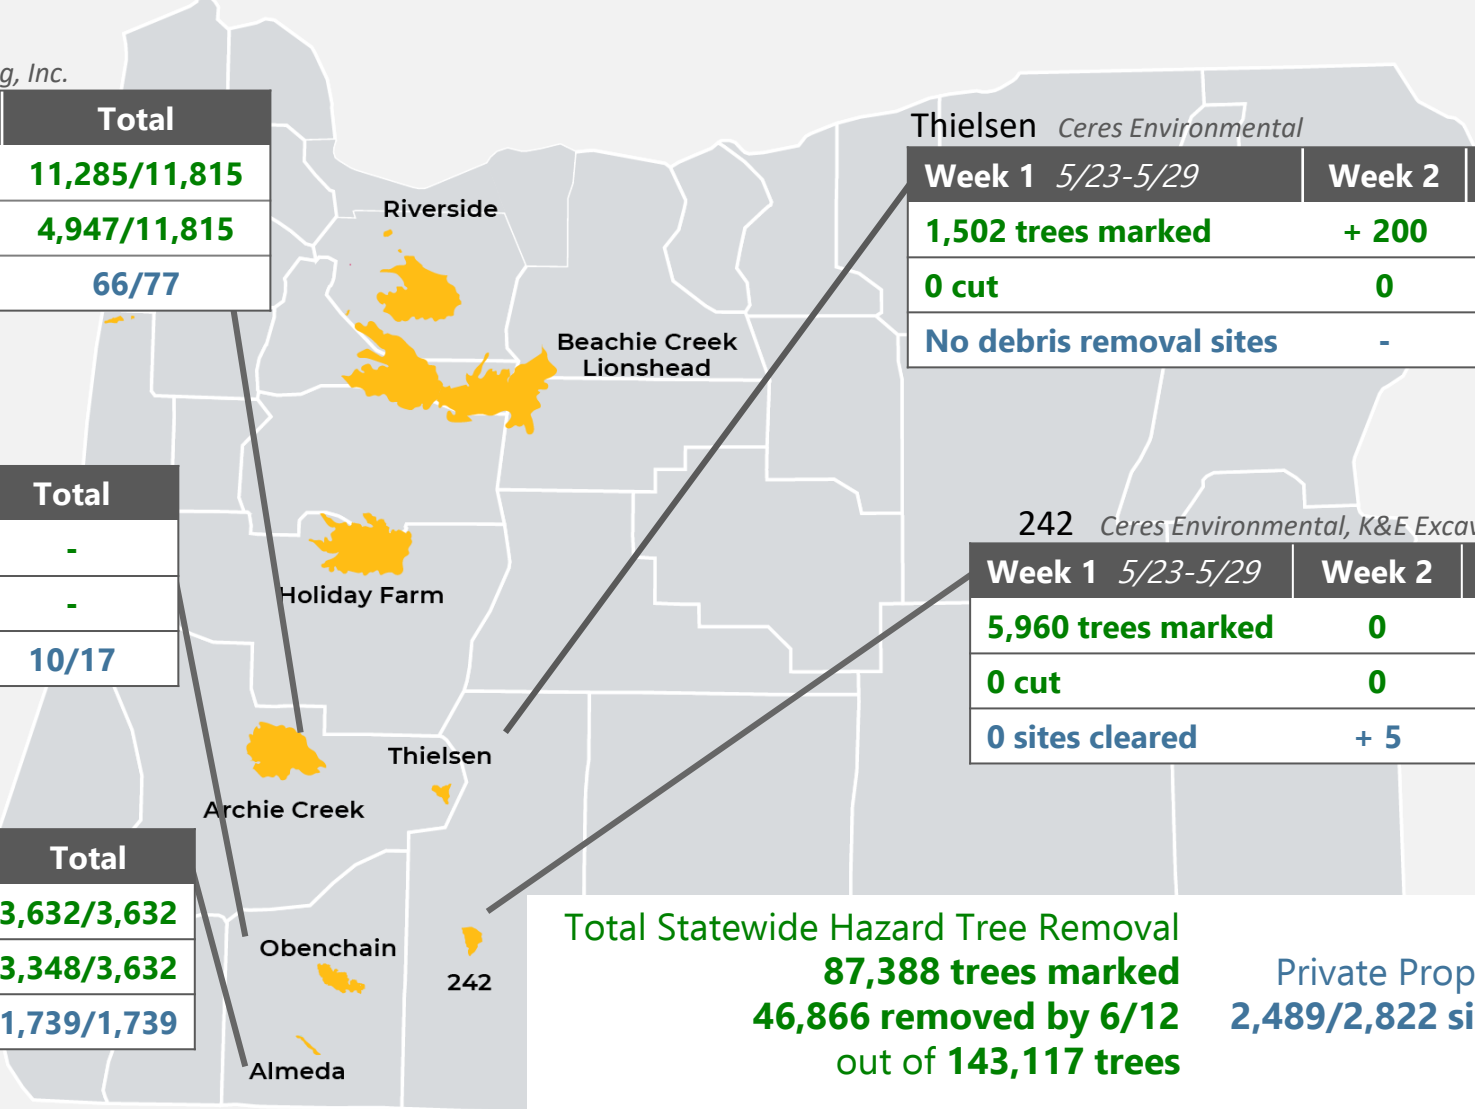

Total Statewide Hazard Tree Removal
87,388 trees marked
46,866 removed by 6/12
 out of **143,117 trees**

Total Statewide Private Property Debris Removal
2,489/2,822 sites cleared by 6/12

Track status with us



Youtube.com/OregonDOT



Twitter.com/OregonOEM



Flickr.com/oregondot

Webpage, interactive status map, dashboard
wildfire.oregon.gov/cleanup

Debris news page
www.DebrisCleanupNews.com



odot.wildfire@odot.state.or.us



Hotline: 503-934-1700
